

# Newhaven Estate - Stage 20, Tarneit

## Level 1 Inspection & Testing Report

Reference: 1120 0404-1



### Prepared for:

BMD Urban

March 2023



**A&Y ASSOCIATES**  
GEOTECHNICAL ENGINEERING CONSULTANTS

# Document Control Record

Prepared by:

**A&Y Associates Pty Ltd**

ABN 92 614 244 665

5/16 Network Drive

Truganina, VIC 3029

**T:** (03) 8754 8325

**E:** info@ayassociates.com.au

**W:** www.ayassociates.com.au

## Document control

<b>Report title</b>	Level 1 Inspection & Testing				
<b>Project reference number</b>	1120 0404-1				
<b>Client</b>	BMD Urban				
<b>Contact name</b>	Jarryd Proctor				
<b>Contact number</b>	0459 805 642				
<b>Contact e-mail</b>	Jarryd.Proctor@bmd.com.au				
<b>Revision</b>	<b>Date</b>	<b>Descriptions/Status</b>	<b>Author</b>	<b>Reviewer</b>	<b>Approver</b>
0	31/03/2023	First Issue	Y Zheng	A Tan	A Tan

## Approver



Alvin Tan

(BE Civil and Infrastructure), MIEAust

Senior Geotechnical Engineer

E: alvin@ayassociates.com.au | M: 0449 288 338



ENGINEERS  
AUSTRALIA  
Professional Engineer  
MEMBER

---

## **Disclaimer**

The findings and conclusions contained in this report are made based on site conditions that existed at the time this work was conducted. The conclusions present in this report are relevant to the conditions of the site and the state of legislation currently enacted as at the date of this report.

Findings and conclusions are made assuming that the soil, groundwater, geological and chemical conditions detailed within this report are accurate and remain applicable to the site at the time of writing. No other warranties are made or intended.

A&Y Associates (A&Y) Pty Ltd has used a degree of skill and care ordinarily exercised by reputable members of our profession practicing in the same or similar locality.

A&Y does not make any representation or warranty that the conclusions in this report will be applicable in the future as there may be changes in the condition of the site, applicable legislation or other factors that would affect the conclusions contained in this report.

This report has been prepared exclusively for use by our client. This report cannot be reproduced without the written authorisation of A&Y and then can only be reproduced in its entirety.

## **Applicability**

This report has been prepared for the benefit for our client with respect to the particular brief given to us and it may not be relied upon in other contexts or for any other purpose without our prior review and agreement.

No responsibility for this report will be taken by A&Y if it is altered in any way, or not reproduced in full.

---

## Contents

<b>1</b>	<b>Introduction.....</b>	<b>3</b>
<b>2</b>	<b>Project Summary .....</b>	<b>3</b>
<b>3</b>	<b>Project Specifications.....</b>	<b>4</b>
<b>4</b>	<b>Subgrade Assessment.....</b>	<b>5</b>
<b>5</b>	<b>Earthworks.....</b>	<b>5</b>
<b>6</b>	<b>Fill Material .....</b>	<b>5</b>
<b>7</b>	<b>Testing.....</b>	<b>6</b>
<b>8</b>	<b>Exclusion .....</b>	<b>6</b>
<b>9</b>	<b>Conclusion .....</b>	<b>6</b>
	<b>Appendix A - Site Plan .....</b>	<b>7</b>
	<b>Appendix B – Test Locations .....</b>	<b>9</b>
	<b>Appendix C – Test Results Summary .....</b>	<b>11</b>
	<b>Appendix D – NATA Test Results .....</b>	<b>13</b>

---

## 1 Introduction

This report presents the results of the Level 1 Inspection and Testing for the construction of the fill platforms located in Newhaven Estate - Stage 20, Tarneit.

## 2 Project Summary

It is understood that BMD Urban require the fill platforms within Stage 20 to be constructed under Level 1 Inspection and Testing undertaken by a Geotechnical Inspection and Testing Authority (GITA).

Level 1 Inspection and Testing, as defined in AS3798-2007 "Guidelines on Earthworks for Commercial and Residential Development," provides for full time inspection of the construction of controlled fill and field and laboratory testing in accordance with AS1289 "Methods of Testing Soils for Engineering Purposes".

The Level 1 inspection was undertaken by a Geotechnician from A&Y Associates over a period of 5 (five) working days from 18<sup>th</sup> of January 2023 to 24<sup>th</sup> of January 2023.

This report is applicable for fill placed by BMD Urban for the following lots located in Newhaven Estate - Stage 20 of Tarneit, as shown in Appendix A – Site Plan.

- Lot 2007 - 2009
- Lot 2011- 2015
- Lot 2018 - 2019
- Lot 2020 - 2045

---

### 3 Project Specifications

The supervision and inspections were performed based on AS3798 and the drawing (ref: Newhaven Estate - Stage 20, Tarneit, Drawing No. 304673CR100-Rev2 by PEET Pty Ltd, Dated 13/07/2022) for the construction works in Newhaven Estate - Stage 20, Tarneit.

A short summary of the requirements is provided below:

- All filling in excess of 200mm depth within the building envelope of allotments shall be undertaken to specifications satisfying the requirements of AS3798.
- Material to be used for fill construction shall satisfy the requirements of AS3798-2007 "Guidelines on Earthworks for Commercial and Residential Developments". Material used shall be free of:
  - Organic soils, such as topsoils, severely root affected subsoil and peat;
  - Contaminated soils;
  - Materials which undergo volume change or loss of strength when disturbed and exposed to moisture;
  - Silts, or materials that have deleterious engineering properties of silt;
  - Fill that contains wood, metal, plastic, boulders, or other deleterious material, in sufficient proportions to affect the required performance of fill;
  - The maximum particle size of any rocks or other lump, within the layer, has not exceeded two-thirds (2/3) of the compacted layer thickness.
- Compaction to achieve a dry density ratio of at least 95% Standard, as the project was classified as **Residential**.

---

## **4 Subgrade Assessment**

The subgrade was assessed by A&Y Associates following the topsoil removal and before any fill was placed. The subgrade assessment was undertaken over 2 Days (two) working days, on the 18<sup>th</sup> of January 2023 and 23<sup>rd</sup> of January 2023 as mentioned in report 1120 0404-1 (SS11).

The exposed subgrade material predominantly comprised of silty clay. No wet or soft patches were found during the inspection. No evidence of deleterious material was found during the inspection.

## **5 Earthworks**

The earthworks for this project included stripping of topsoil, removing of tree roots, proof rolling the subgrade and placement and compaction of fill to construct engineered platforms.

Based on design plans and site inspection, it appears that the fill thickness placed is approximately 200-600mm. The fill layers or thickness nominated in this report are provided as a guide on the amounts of fill placed and do not necessarily reflect an accurate survey of the fill levels.

## **6 Fill Material**

The fill material used for the platform consisted of imported material. The imported material was predominantly comprising of Silty Clay with gravels.

---

## 7 Testing

Field density testing was undertaken on the compacted fill at a frequency of a minimum of 3 tests per lot (AS3798 Table 8.1).

Tests were performed using a Nuclear Density Gauge for field density determination as per AS 1289.5.8.1. Testing was completed at a minimum rate of 3 field density tests per day's production based on the minimum requirements of AS 3798-2007 and taken from each layer of fill placed.

A total of 15 field density tests were performed during the earthworks. All of the test results met the specified compaction requirement of 95% Standard Compaction.

The locations of the 15 field density tests are shown in Appendix B – Test Locations. A summary of the test results obtained from the field density testing is presented in Appendix C – Test Results Summary. The laboratory test reports of the field density tests are presented in Appendix D – NATA Test Results.

## 8 Exclusion

A&Y Associates was not involved in monitoring and testing the following works and as such are not included in the Level 1 report.

- Any trenches excavated and backfilled on site for the installation of underground services such as sewers, electrical conduits, water mains etc.
- Footpaths in front of the lots that may be excavated and filled after the Level 1 supervision conducted by A&Y Associates.
- Uncontrolled fill and topsoil that may have been placed as part of the landscaping of the site following the completion of the engineered fill construction.

## 9 Conclusion

On the completion of the earthworks and after analysing the materials used, it has been concluded that the filling procedure conducted by BMD Urban appears to be consistent with the requirements of AS 3798 in regards to the placement of fill materials on a project under Level 1 Supervision and in accordance with the project specification as provided to A&Y Associates.




---

# **Appendix A - Site Plan**



Area Inspected


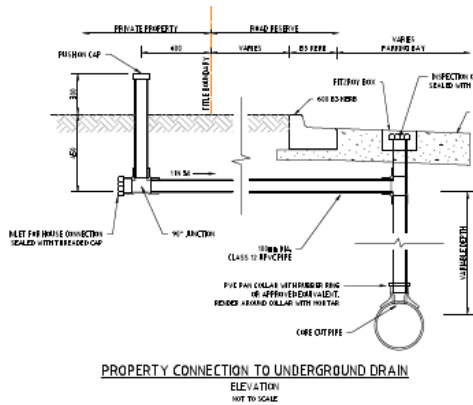


NOTE: PROVIDE AN INSPECTION OPENING TO BE LOCATED IN PARKING BAY WITHIN PARCELS BY FAT LOTS 2012, 2013 & 2015, REFER DETAIL ABOVE FOR PROPERTY CONNECTION TO UNDERGROUND DRAIN.

**WARNING**  
BEWARE OF UNDERGROUND OVERHEAD SERVICES  
THE LOCATION OF SERVICES ARE APPROXIMATE ONLY AND THEIR EXACT POSITION SHOULD BE FOUND ON SITE. NO GUARANTEE IS GIVEN THAT ALL EXISTING SERVICES ARE SHOWN. SPECIAL CONSIDERATION SHOULD BE GIVEN TO CONSTRUCTION PROCEDURES TAKEN IN HIGH-VOLTAGY TRANSMISSION LINES.



Rev	Amendments	Assessed	Date
1	ISSUED FOR APPROVAL	M.H.	13/07/22
2	ISSUED FOR CONSTRUCTION	M.H.	31/01/23
3	DETAILS AMENDED PER COUNCIL COMMENTS	M.H.	13/07/22
4	ISSUED FOR APPROVAL	M.H.	17/12/21



**NEWHAVEN ESTATE STAGE 20 ROAD AND DRAINAGE FACE PLAN**  
WINDHAM CITY COUNCIL  
PEET NO. 1896 PTY LTD  
**CONSTRUCTION 304673CR200 1**

**PROJECT:**  
Newhaven Estate Stage 20

**CLIENT:**  
BMD Urban

**SITE PLAN SKETCH—NOT TO SCALE**



**LOCATION:**  
Tarneit

**PROJECT No:**  
1120 0404-1

---



## **Appendix B – Test Locations**



Indicative Test Location



Rev	Amendments	Assessed	Date
1	ISSUED FOR APPROVAL	M.H.	13/07/22
2	ISSUED FOR CONSTRUCTION	M.H.	31/01/23
3	DETAILS AMENDED PER COUNCIL COMMENTS	M.H.	13/07/22
4	ISSUED FOR APPROVAL	M.H.	17/03/21



**NEWHAVEN ESTATE STAGE 20 ROAD AND DRAINAGE FACE PLAN**  
WINDHAM CITY COUNCIL  
PEET NO. 1836 PTY LTD  
**CONSTRUCTION 304673CR200 1**

**PROJECT:**  
Newhaven Estate Stage 20

**LOCATION:**  
Tarneit

**CLIENT:**  
BMD Urban

**PROJECT No:**  
1120 0404-1

**SITE PLAN SKETCH—NOT TO SCALE**



---

# **Appendix C – Test Results Summary**

Project No		1120 0404-1			Client	BMD Urban				
Project Name		Newhaven Estate Stage 20			Specification			Density Ratio $\geq$ 95% of Peak Wet Density		
Location		Tarneit								
Test No	Retest of Test	Date	Location	Layer	Oversize	Density Ratio	Moisture Ratio	Moisture Variation	Pass / Fail	Retest
#	#		Lot #	#	%	%	%	%		Pass / Fail
1	-	18/01/2023	-	1	12.6	98.5	100.0	0.0	Pass	-
2	-	18/01/2023	-	1	14.2	97.5	103.0	0.5	Pass	-
3	-	18/01/2023	-	1	10.2	98.5	101.5	0.0	Pass	-
4	-	19/01/2023	-	1	11.1	97.0	99.5	0.0	Pass	-
5	-	19/01/2023	-	1	14.0	97.5	102.0	0.0	Pass	-
6	-	19/01/2023	-	2	12.7	98.0	102.5	0.0	Pass	-
7	-	20/01/2023	-	2	12.8	97.0	101.0	0.0	Pass	-
8	-	20/01/2023	-	3	14.6	96.5	100.5	0.0	Pass	-
9	-	20/01/2023	-	3	13.5	98.5	100.0	0.0	Pass	-
10	-	23/01/2023	-	1	13.0	97.5	102.0	0.5	Pass	-
11	-	23/01/2023	-	1	14.0	96.0	101.0	0.0	Pass	-
12	-	23/01/2023	-	1	15.1	97.0	99.5	0.0	Pass	-
13	-	24/01/2023	-	2	13.5	99.5	101.5	0.0	Pass	-
14	-	24/01/2023	-	2	14.4	97.0	96.0	-0.5	Pass	-
15	-	24/01/2023	-	2	12.9	97.0	100.5	0.0	Pass	-

\*\* Negative (-) value indicates that the field moisture content is drier than the optimum moisture content (OMC)

\*\* Positive (+) value indicates that the field moisture content is wetter than the optimum moisture content (OMC)

---

## **Appendix D – NATA Test Results**

## Field Density Test Results AS1289.5.7.1

<b>Client:</b>	BMD Urban	<b>Job No:</b>	BMD2712
<b>Project:</b>	Newhaven Estate - Stage 20 (Level 1)	<b>Report:</b>	1
<b>Location:</b>	Tarneit		

Sample No	1	2	3			
Date Tested	18/01/2023	18/01/2023	18/01/2023			
Time Tested	PM	PM	PM			

Test Location	Refer to Plan	Refer to Plan	Refer to Plan			
Level/Layer	1	1	1			
Layer Thickness	mm 200	mm 200	mm 200			
Test Depth	mm 175	mm 175	mm 175			
Field Wet Density	t/m <sup>3</sup> 1.97	t/m <sup>3</sup> 2.03	t/m <sup>3</sup> 1.99			
Field Moisture Content	% 20.0	% 20.6	% 21.3			
Material:	Site Derived Clay	Site Derived Clay	Site Derived Clay			



  

Oversize Material	WET, %	12.6	14.2	10.2		
Sieve Size	mm	37.5	37.5	37.5		
Peak Converted Wet Density	t/m <sup>3</sup>	1.94	2.04	1.98		
Optimum Moisture Content	%	20	20	21		

<b>Moisture Ratio</b>	%	100	103	101.5		
<b>Moisture Variation from OMC</b>	%	0.0	0.5	0.0		
<b>Density Ratio</b>	%	98.5	97.5	98.5		


<b>Specification:</b>	95% STD	<b>Test Selection:</b>	N/A
<b>Notes:</b>	Ref: 1120 0404-1 (SI01)		
<b>Test Method</b>	AS1289 5.8.1, 5.7.1, 2.1.1, 1.1	<b>Sampling Method:</b>	AS 1289 1.2.1 6.4(b)

 <small>WORLD RECOGNISED ACCREDITATION</small>	<p>NATA Accredited Laboratory No. 20172</p> <p>Accreditation for compliance with ISO/IEC 17025 - Testing</p>	<p>Approved Signatory:</p> 	
		<p>David Burns</p>	
		<p>Date: 27/03/2023</p>	





Test Location

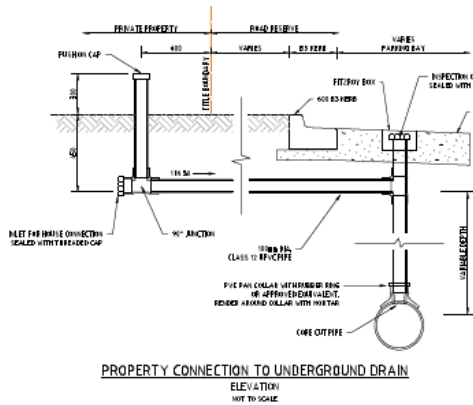

**WARNING**  
BEWARE OF UNDERGROUND OVERHEAD SERVICES  
THE LOCATION OF SERVICES ARE APPROXIMATE ONLY AND THEIR  
EXACT POSITION SHOULD BE FOUND ON SITE, NO GUARANTEES  
BE GIVEN THAT ALL EXISTING SERVICES ARE SHOWN, SPECIAL  
CONSIDERATION SHOULD BE GIVEN TO CONSTRUCTION PROCEDURES  
UNDER HIGH-VOLTAGY TRANSMISSION LINES.



Rev	Description	Assessed	Date
1	ISSUED FOR CONSTRUCTION	M.H.	15/07/22
2	ISSUED FOR APPROVAL	M.H.	17/12/21



**NEWHAVEN ESTATE STAGE 20 ROAD AND DRAINAGE FACE PLAN**  
WINDHAM CITY COUNCIL  
PEET NO. 1836 PTY LTD  
**CONSTRUCTION** 304673CR200 1

**PROJECT:**  
Newhaven Estate – Stage 20 (Level 1)

**CLIENT:**  
BMD Urban

**DATE:**  
18/01/2023

**LOCATION:**  
Tarnet

**PROJECT No:**  
1120 0404-1 (SI01)

**SITE PLAN SKETCH—NOT TO SCALE**



## Field Density Test Results AS1289.5.7.1

<b>Client:</b>	BMD Urban	<b>Job No:</b>	BMD2712
<b>Project:</b>	Newhaven Estate - Stage 20 (Level 1)	<b>Report:</b>	2
<b>Location:</b>	Tarneit		

Sample No	4	5	6			
Date Tested	19/01/2023	19/01/2023	19/01/2023			
Time Tested	PM	PM	PM			

Test Location	Refer to Plan	Refer to Plan	Refer to Plan			
Level/Layer	1	1	2			
Layer Thickness	mm 200	mm 200	mm 200			
Test Depth	mm 175	mm 175	mm 175			
Field Wet Density	t/m <sup>3</sup> 2.01	t/m <sup>3</sup> 2.04	t/m <sup>3</sup> 1.98			
Field Moisture Content	% 22.4	% 20.9	% 19.5			
Material:	Site Derived Clay	Site Derived Clay	Site Derived Clay			

Oversize Material	WET, % 11.1	14.0	12.7			
Sieve Size	mm 37.5	mm 37.5	mm 37.5			
Peak Converted Wet Density	t/m <sup>3</sup> 2.03	t/m <sup>3</sup> 2.04	t/m <sup>3</sup> 1.96			
Optimum Moisture Content	% 22.5	% 20.5	% 19			

<b>Moisture Ratio</b>	%	99.5	102	102.5		
<b>Moisture Variation from OMC</b>	%	0.0	0.0	0.0		
<b>Density Ratio</b>	%	97.0	97.5	98.0		

<b>Specification:</b>	95% STD	<b>Test Selection:</b>	N/A
<b>Notes:</b>	Ref: 1120 0404-1 (SI02)		
<b>Test Method</b>	AS1289 5.8.1, 5.7.1, 2.1.1, 1.1	<b>Sampling Method:</b>	AS 1289 1.2.1 6.4(b)



NATA Accredited Laboratory No. 20172  
Accreditation for compliance with ISO/IEC 17025 - Testing

Approved Signatory:



David Burns

Date: 27/03/2023



# Field Density Test Results

## AS1289.5.7.1

<b>Client:</b>	BMD Urban	<b>Job No:</b>	BMD2712
<b>Project:</b>	Newhaven Estate - Stage 20 (Level 1)	<b>Report:</b>	3
<b>Location:</b>	Tarneit		

Sample No	7	8	9			
Date Tested	20/01/2023	20/01/2023	20/01/2023			
Time Tested	PM	PM	PM			

Test Location	Refer to Plan	Refer to Plan	Refer to Plan			
Level/Layer	2	3	3			
Layer Thickness	mm 200	200	200			
Test Depth	mm 175	175	175			
Field Wet Density	t/m <sup>3</sup> 1.97	2.02	2.05			
Field Moisture Content	% 20.2	21.1	19.0			
Material:	Site Derived Clay	Site Derived Clay	Site Derived Clay			

Oversize Material	WET, %	12.8	14.6	13.5		
Sieve Size	mm	37.5	37.5	37.5		
Peak Converted Wet Density	t/m <sup>3</sup>	1.98	2.04	2.03		
Optimum Moisture Content	%	20	21	19		

<b>Moisture Ratio</b>	%	101	100.5	100		
<b>Moisture Variation from OMC</b>	%	0.0	0.0	0.0		
<b>Density Ratio</b>	%	97.0	96.5	98.5		

<b>Specification:</b>	95% STD	<b>Test Selection:</b>	N/A
<b>Notes:</b>	Ref: 1120 0404-1 (SI03)		
<b>Test Method</b>	AS1289 5.8.1, 5.7.1, 2.1.1, 1.1	<b>Sampling Method:</b>	AS 1289 1.2.1 6.4(b)



NATA Accredited Laboratory No. 20172  
Accreditation for compliance with ISO/IEC 17025 - Testing

Approved Signatory:




David Burns

Date: 27/03/2023





Test Location

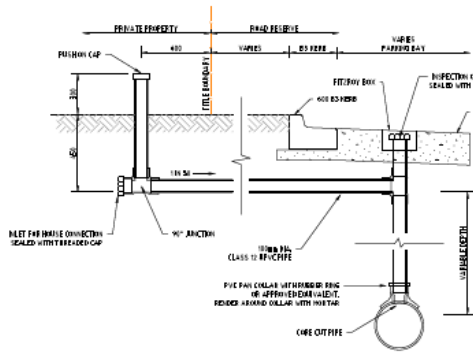


**NOTES:**  
 1. REFER TO ALL INSPECTION OPENINGS TO BE LOCATED BY PROPERTY OWNER WITHIN PARKING BAY FAY LOTS 2012, 2013 & 2015, REFER DETAIL ABOVE FOR PROPERTY CONNECTION TO UNDERGROUND DRAIN.

**WARNING**  
 BEWARE OF UNDERGROUND OVERHEAD SERVICES  
 THE LOCATION OF SERVICES ARE APPROXIMATE ONLY AND THEIR EXACT POSITION SHOULD BE FOUND ON SITE, NO GUARANTEE IS GIVEN THAT ALL EXISTING SERVICES ARE SHOWN. SPECIAL CONSIDERATION SHOULD BE GIVEN TO CONSTRUCTION PROCEDURES TAKEN TO AVOID ELECTRICITY TRANSMISSION LINES.



Rev	Amendments	Assessed	Date
1	ISSUED FOR CONSTRUCTION	M.H.	15/07/22
2	ISSUED FOR APPROVAL	M.H.	17/12/21



**spiire**  
 LE 414 LA TROSE STREET PO BOX 1004 MELBOURNE  
 VICTORIA 3004 AUSTRALIA T 61 3 9000 7000  
 spiire.com.au ABN 55 000 029 635

**PEET**  
 Checked J. KOEHLER  
 Date 17/12/21

**NEWHAVEN ESTATE  
 STAGE 20  
 ROAD AND DRAINAGE  
 FACE PLAN  
 WINDHAM CITY COUNCIL  
 PEET NO.1896 PTY LTD**

**CONSTRUCTION 304673CR200 1**

**PROJECT:**  
 Newhaven Estate – Stage 20 (Level 1)

**LOCATION:**  
 Tarneit

**CLIENT:**  
 BMD Urban

**PROJECT No:**  
 1120 0404-1 (SI03)

**DATE:**  
 20/01/2023

**SITE PLAN SKETCH—NOT TO SCALE**



# Field Density Test Results

## AS1289.5.7.1

<b>Client:</b>	BMD Urban	<b>Job No:</b>	BMD2712
<b>Project:</b>	Newhaven Estate - Stage 20 (Level 1)	<b>Report:</b>	4
<b>Location:</b>	Tarneit		

Sample No	10	11	12			
Date Tested	23/01/2023	23/01/2023	23/01/2023			
Time Tested	PM	PM	PM			

Test Location	Refer to Plan	Refer to Plan	Refer to Plan			
Level/Layer	1	1	1			
Layer Thickness	mm 200	mm 200	mm 200			
Test Depth	mm 175	mm 175	mm 175			
Field Wet Density	t/m <sup>3</sup> 2.07	t/m <sup>3</sup> 2.02	t/m <sup>3</sup> 1.99			
Field Moisture Content	% 20.9	% 19.7	% 21.9			
Material:	Site Derived Clay	Site Derived Clay	Site Derived Clay			

Oversize Material	WET, %	13.0	14.0	15.1		
Sieve Size	mm	37.5	37.5	37.5		
Peak Converted Wet Density	t/m <sup>3</sup>	2.08	2.05	1.99		
Optimum Moisture Content	%	20.5	19.5	22		

<b>Moisture Ratio</b>	%	102	101	99.5		
<b>Moisture Variation from OMC</b>	%	0.5	0.0	0.0		
<b>Density Ratio</b>	%	97.5	96.0	97.0		

<b>Specification:</b>	95% STD	<b>Test Selection:</b>	N/A
<b>Notes:</b>	Ref: 1120 0404-1 (SI04)		
<b>Test Method</b>	AS1289 5.8.1, 5.7.1, 2.1.1, 1.1	<b>Sampling Method:</b>	AS 1289 1.2.1 6.4(b)



NATA Accredited Laboratory No. 20172  
Accreditation for compliance with ISO/IEC 17025 - Testing

Approved Signatory:



David Burns

Date: 27/03/2023



## Field Density Test Results AS1289.5.7.1

<b>Client:</b>	BMD Urban	<b>Job No:</b>	BMD2712
<b>Project:</b>	Newhaven Estate - Stage 20 (Level 1)	<b>Report:</b>	5
<b>Location:</b>	Tarneit		

Sample No	13	14	15			
Date Tested	24/01/2023	24/01/2023	24/01/2023			
Time Tested	PM	PM	PM			

Test Location	Refer to Plan	Refer to Plan	Refer to Plan			
Level/Layer	2	2	2			
Layer Thickness	mm 200	mm 200	mm 200			
Test Depth	mm 175	mm 175	mm 175			
Field Wet Density	t/m <sup>3</sup> 2.06	t/m <sup>3</sup> 2.03	t/m <sup>3</sup> 2.00			
Field Moisture Content	% 20.8	% 21.6	% 23.6			
Material:	Site Derived Clay	Site Derived Clay	Site Derived Clay			

Oversize Material	WET, %	13.5	14.4	12.9		
Sieve Size	mm	37.5	37.5	37.5		
Peak Converted Wet Density	t/m <sup>3</sup>	2.02	2.04	2.01		
Optimum Moisture Content	%	20.5	22.5	23.5		

<b>Moisture Ratio</b>	%	101.5	96	100.5		
<b>Moisture Variation from OMC</b>	%	0.0	-0.5	0.0		
<b>Density Ratio</b>	%	99.5	97.0	97.0		

<b>Specification:</b>	95% STD	<b>Test Selection:</b>	N/A
<b>Notes:</b>	Ref: 1120 0404-1 (SI05)		
<b>Test Method</b>	AS1289 5.8.1, 5.7.1, 2.1.1, 1.1	<b>Sampling Method:</b>	AS 1289 1.2.1 6.4(b)



NATA Accredited Laboratory No. 20172  
Accreditation for compliance with ISO/IEC 17025 - Testing

Approved Signatory:




David Burns

Date: 27/03/2023





Test Location

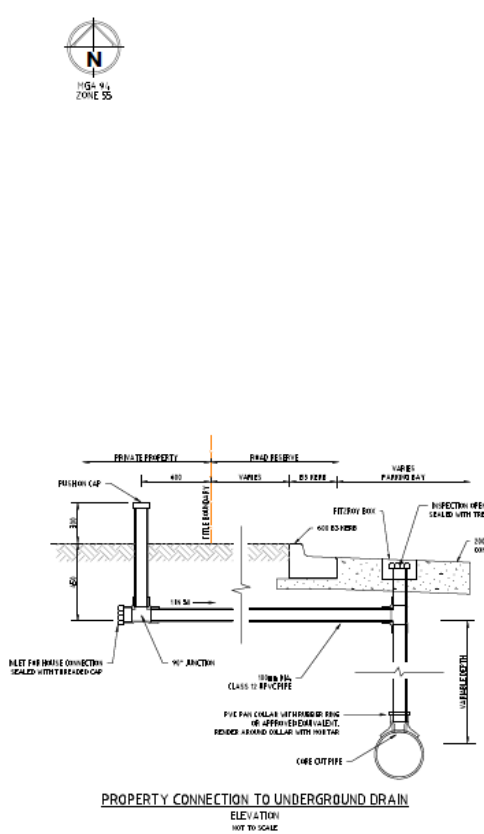


PROPERTY CONNECTION TO UNDERGROUND DRAIN  
ELEVATION  
NOT TO SCALE

**NOTE:**  
FOR ALL INSPECTION OPENINGS TO BE LOCATED IN PARADEWAY WITHIN PARADEWAY PAVEMENTS 2012, 2013 & 2015, REFER DETAIL ABOVE FOR PROPERTY CONNECTION TO UNDERGROUND DRAIN.

**WARNING**  
BEWARE OF UNDERGROUND OVERHEAD SERVICES  
THE LOCATION OF SERVICES ARE APPROXIMATE ONLY AND THEIR EXACT POSITION SHOULD BE FOUND ON SITE, IN GUARANTEE OF THIS ALL EXISTING SERVICES ARE SHOWN. SPECIAL CONSIDERATION SHOULD BE GIVEN TO CONSTRUCTION PROCEDURES TAKEN TO PREVENT DAMAGE TO TRANSMISSION LINES.



Rev	Amendments	Assessed	Date
1	ISSUED FOR CONSTRUCTION	M.H.	15/07/22
2	ISSUED FOR APPROVAL	M.H.	17/12/21



**spiire**  
 LE 414 LA TROSE STREET PO BOX 1004 MELBOURNE  
 VICTORIA 3004 AUSTRALIA T 61 3 9000 7000  
 spiire.com.au ABN 55 000 029 635

**PEET**  
 Designed  
 P. CLIFTON  
 M. HOLMES  
 Checked  
 J. KOEHLER  
 Date  
 17/12/21

**NEWHAVEN ESTATE  
 STAGE 20  
 ROAD AND DRAINAGE  
 FACE PLAN  
 WINDHAM CITY COUNCIL  
 PEET NO. 1896 PTY LTD**  
**CONSTRUCTION 304673CR200 1**

**PROJECT:**  
 Newhaven Estate – Stage 20 (Level 1)

**LOCATION:**  
 Tarneit

**CLIENT:**  
 BMD Urban

**PROJECT No:**  
 1120 0404-1 (SI05)

**DATE:**  
 24/01/2023

**SITE PLAN SKETCH—NOT TO SCALE**

